

Window & Door Replacement

FIELD REPORT #

3

Date: 30-Oct-20

Dunes Of Panama
7205 Thomas Dr
Panama City Beach, FL 32408

WEATHER Cool, Sunny
TEMP RANGE 54-69

WORK IN PROGRESS

Window & Sliding Glass Door Replacement
Storm Prep

SITE PERSONNEL

Pendleton + Bowman, Inc.
SunCoast Restoration & Waterproofing
VHI Windows & Doors
PGT





Hurricane Zeta came in to the west of us this week, however, rain & gusty winds were forecasted. SunCoast put in extra effort to ensure job site was cleaned up & secure.

Building B & C are able to use a lift to be able to remove old materials and bring them to the dumpsters. Frames are taken off & put into one dumpster for recycling. The glass is put into the other dumpster and crushed by the forks of the lift for disposal.



PENDLETON + BOWMAN, INC.

Permits have been posted in each building in the elevator lobby for high visibility.

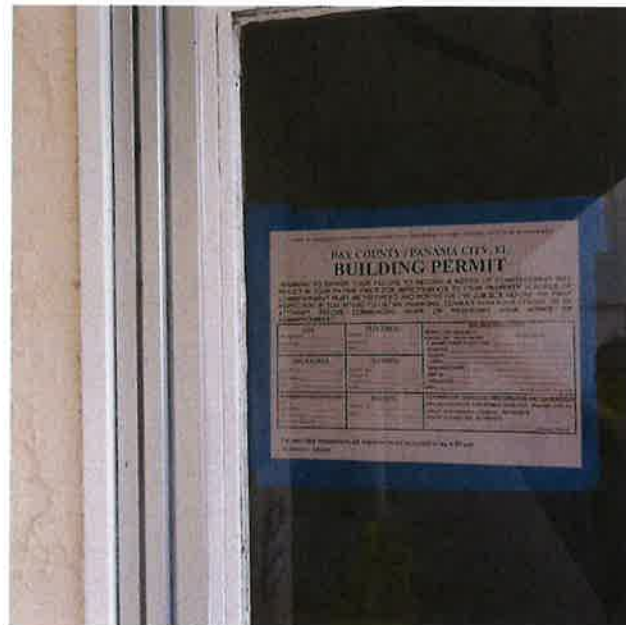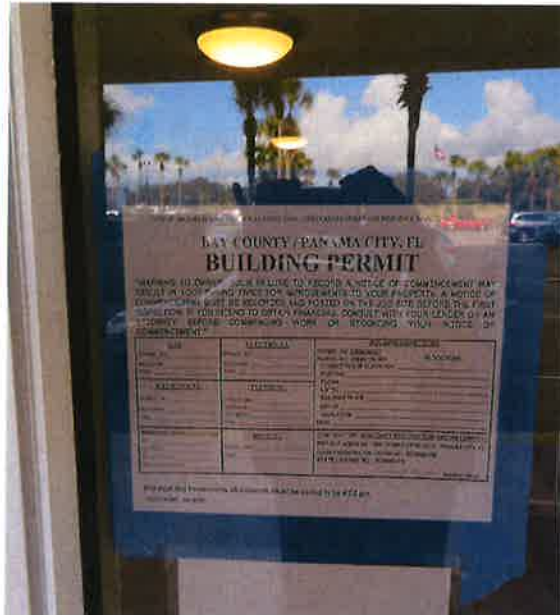

As we make our way down the building the new sliding glass windows are brightening up the overall appearance of the building.



As was discussed previously the CoVid pandemic has affected our material deliveries. We are expecting the small sliders on the ends to be delivered on 11/25/20. The schedule has been revised so that we start on the units that have all materials already on site.

Window installation is going smoothly. Once old window & frames are removed, the rough opening is then cleaned and new windows installed. The units with the floor to ceiling windows are placed in a bed of sealant to ensure a water tight seal. When the windows have been properly anchored in backer rod is installed and then the final layer of the NP150 sealant. The sealant must be given 24 hours to cure out & then it is painted to match the wall color. The bottom layer of sealant is a stone color to help hide the appearance of dirt & debris.

